

17 CUP 1082

17 CUP

RECEIVED

SEP 25 2017

PLANNING & DESIGN SERVICES

# 2017 FALL PROJECT – TRINITY HOUSE DAYCARE CENTER

## SITE LEADERS – SCOTT SHAVER



- Renovate kitchen
  - Move non-load bearing wall 3 feet
  - Add new range and exhaust hood
  - Add new cabinets
- Bathroom upgrade
  - Replace 2 adult toilets with child toilets
- Build storage shelves
  - Add new “cubby” shelving
- Natural playground
  - Move existing parking lot to right of building.
  - Change existing parking lot into playground with many natural play areas.
  - Install shade sail for shade cover.
- Install 6’ perimeter fencing



**GE APPLIANCES**  
a Haier company

RECEIVED

SEP 25 2017  
PLANNING &  
DESIGN SERVICES

# Sail Shade Team



## TEAM LEADER:

Rob Willy                      502-381-5367  
rob.willy@geappliances.com

### Wed: 4 people

Scope: Drill 4 holes, set and level 4 steel poles

Equipment: Post-hole digger (12" with extension), bobcat with bucket and forks

Materials: Crushed limestone, poles (Popp Machine), wood for bracing

Volunteer Tools: shovels, gloves, rake, wheelbarrow, 8' step-ladder, 4' level

### Thurs: 4 people

Scope: Pour concrete from ready-mix truck or bags (TBD)

Equipment: bobcat with forks

Volunteer Tools: shovels, gloves, rake, wheelbarrow, concrete finishing tools, hose, 4' level

### Fri: 6 people (4 sails, 2 painters)

Scope: Install sails and prime/paint posts

Volunteer Tools: shovels, gloves, rake, 8' step-ladder, sawzall, crescent wrench, vise-grips, screw-driver


RECEIVED

SEP 25 2017

PLANNING &  
DESIGN SERVICES

17 CUP 1082

# Post Layout

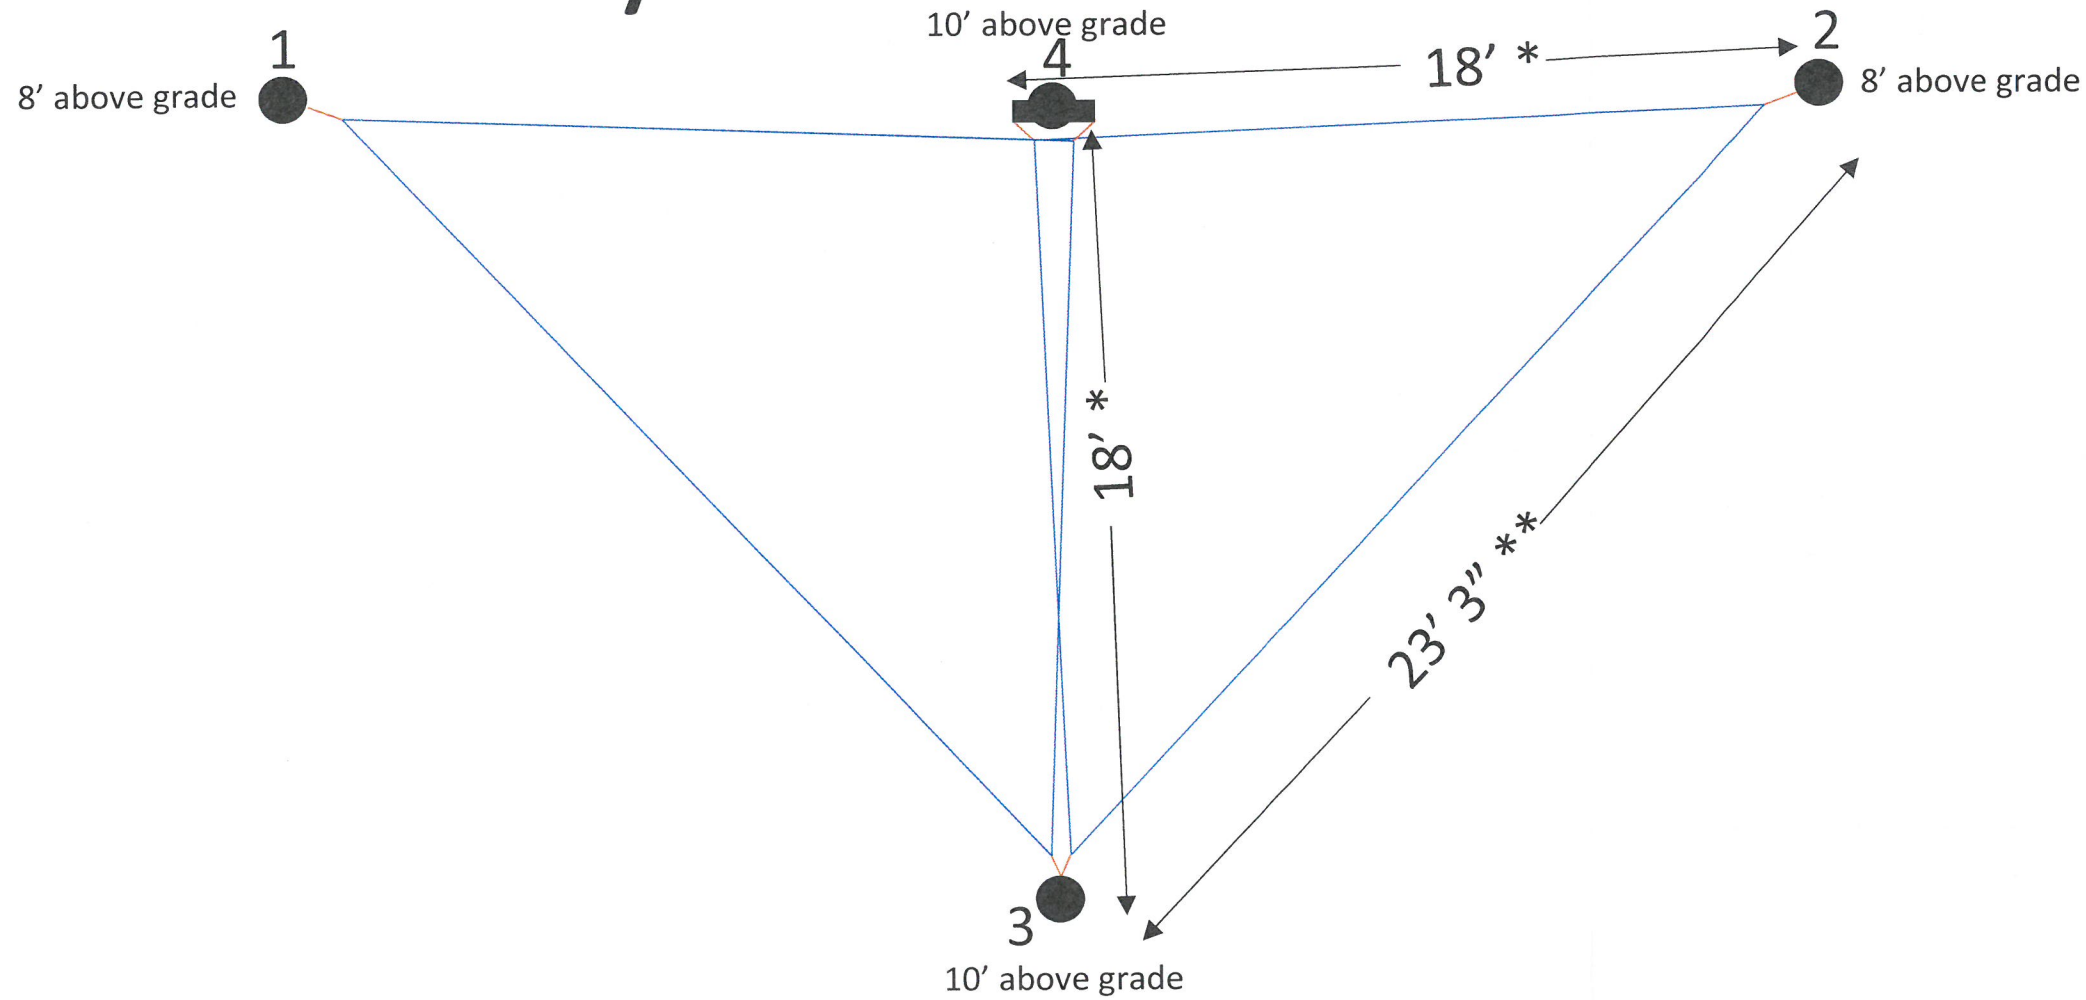

\* 18' = 15' sail corner to corner + 2x18" of tensioning chain

\*\* 23' 3" = 21' 3" sail corner to corner + 2x18" of tensioning chain

RECEIVED

SEP 25 2017  
PLANNING &  
DESIGN SERVICES

17 CUP 1082
